


City of Duvall: 3rd Avenue NE Reconstruction



City of Duvall: 3rd Avenue NE Reconstruction

ID	Task Name	Duration	Start	Finish	Predecessors	3rd Quarter		4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			2nd Quarter		
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	
22	Structural Design	20 days	Fri 10/27/23	Mon 11/27/23	19FS+5 days																							
23	Final Stormwater TIR	15 days	Wed 11/8/23	Thu 11/30/23	20FF+3 days																							
24	City & WSDOT (if using Fed Funds) Review and Comment	20 days	Tue 11/28/23	Tue 12/26/23	20																							
25	Bid Documents	15 days	Wed 12/27/23	Thu 1/18/24	24																							
26	Advertisement	3 wks	Tue 1/23/24	Mon 2/12/24	25FS+2 days																							
27	Right Of Way Acquisition	9 mons	Tue 3/21/23	Mon 12/4/23	9FS+20 days																							
28	Environmental Permitting	200 days?	Tue 2/21/23	Mon 12/4/23																								
29	Permit Applications	3 mons	Tue 2/21/23	Mon 5/15/23	9																							
30	Permit Review	7 mons	Tue 5/16/23	Mon 12/4/23	29																							
31	NEPA Documentation (if Fed Funds obtained) 1-2 months																											
32	NEPA Review (if Fed Funds) 1 year or longer																											

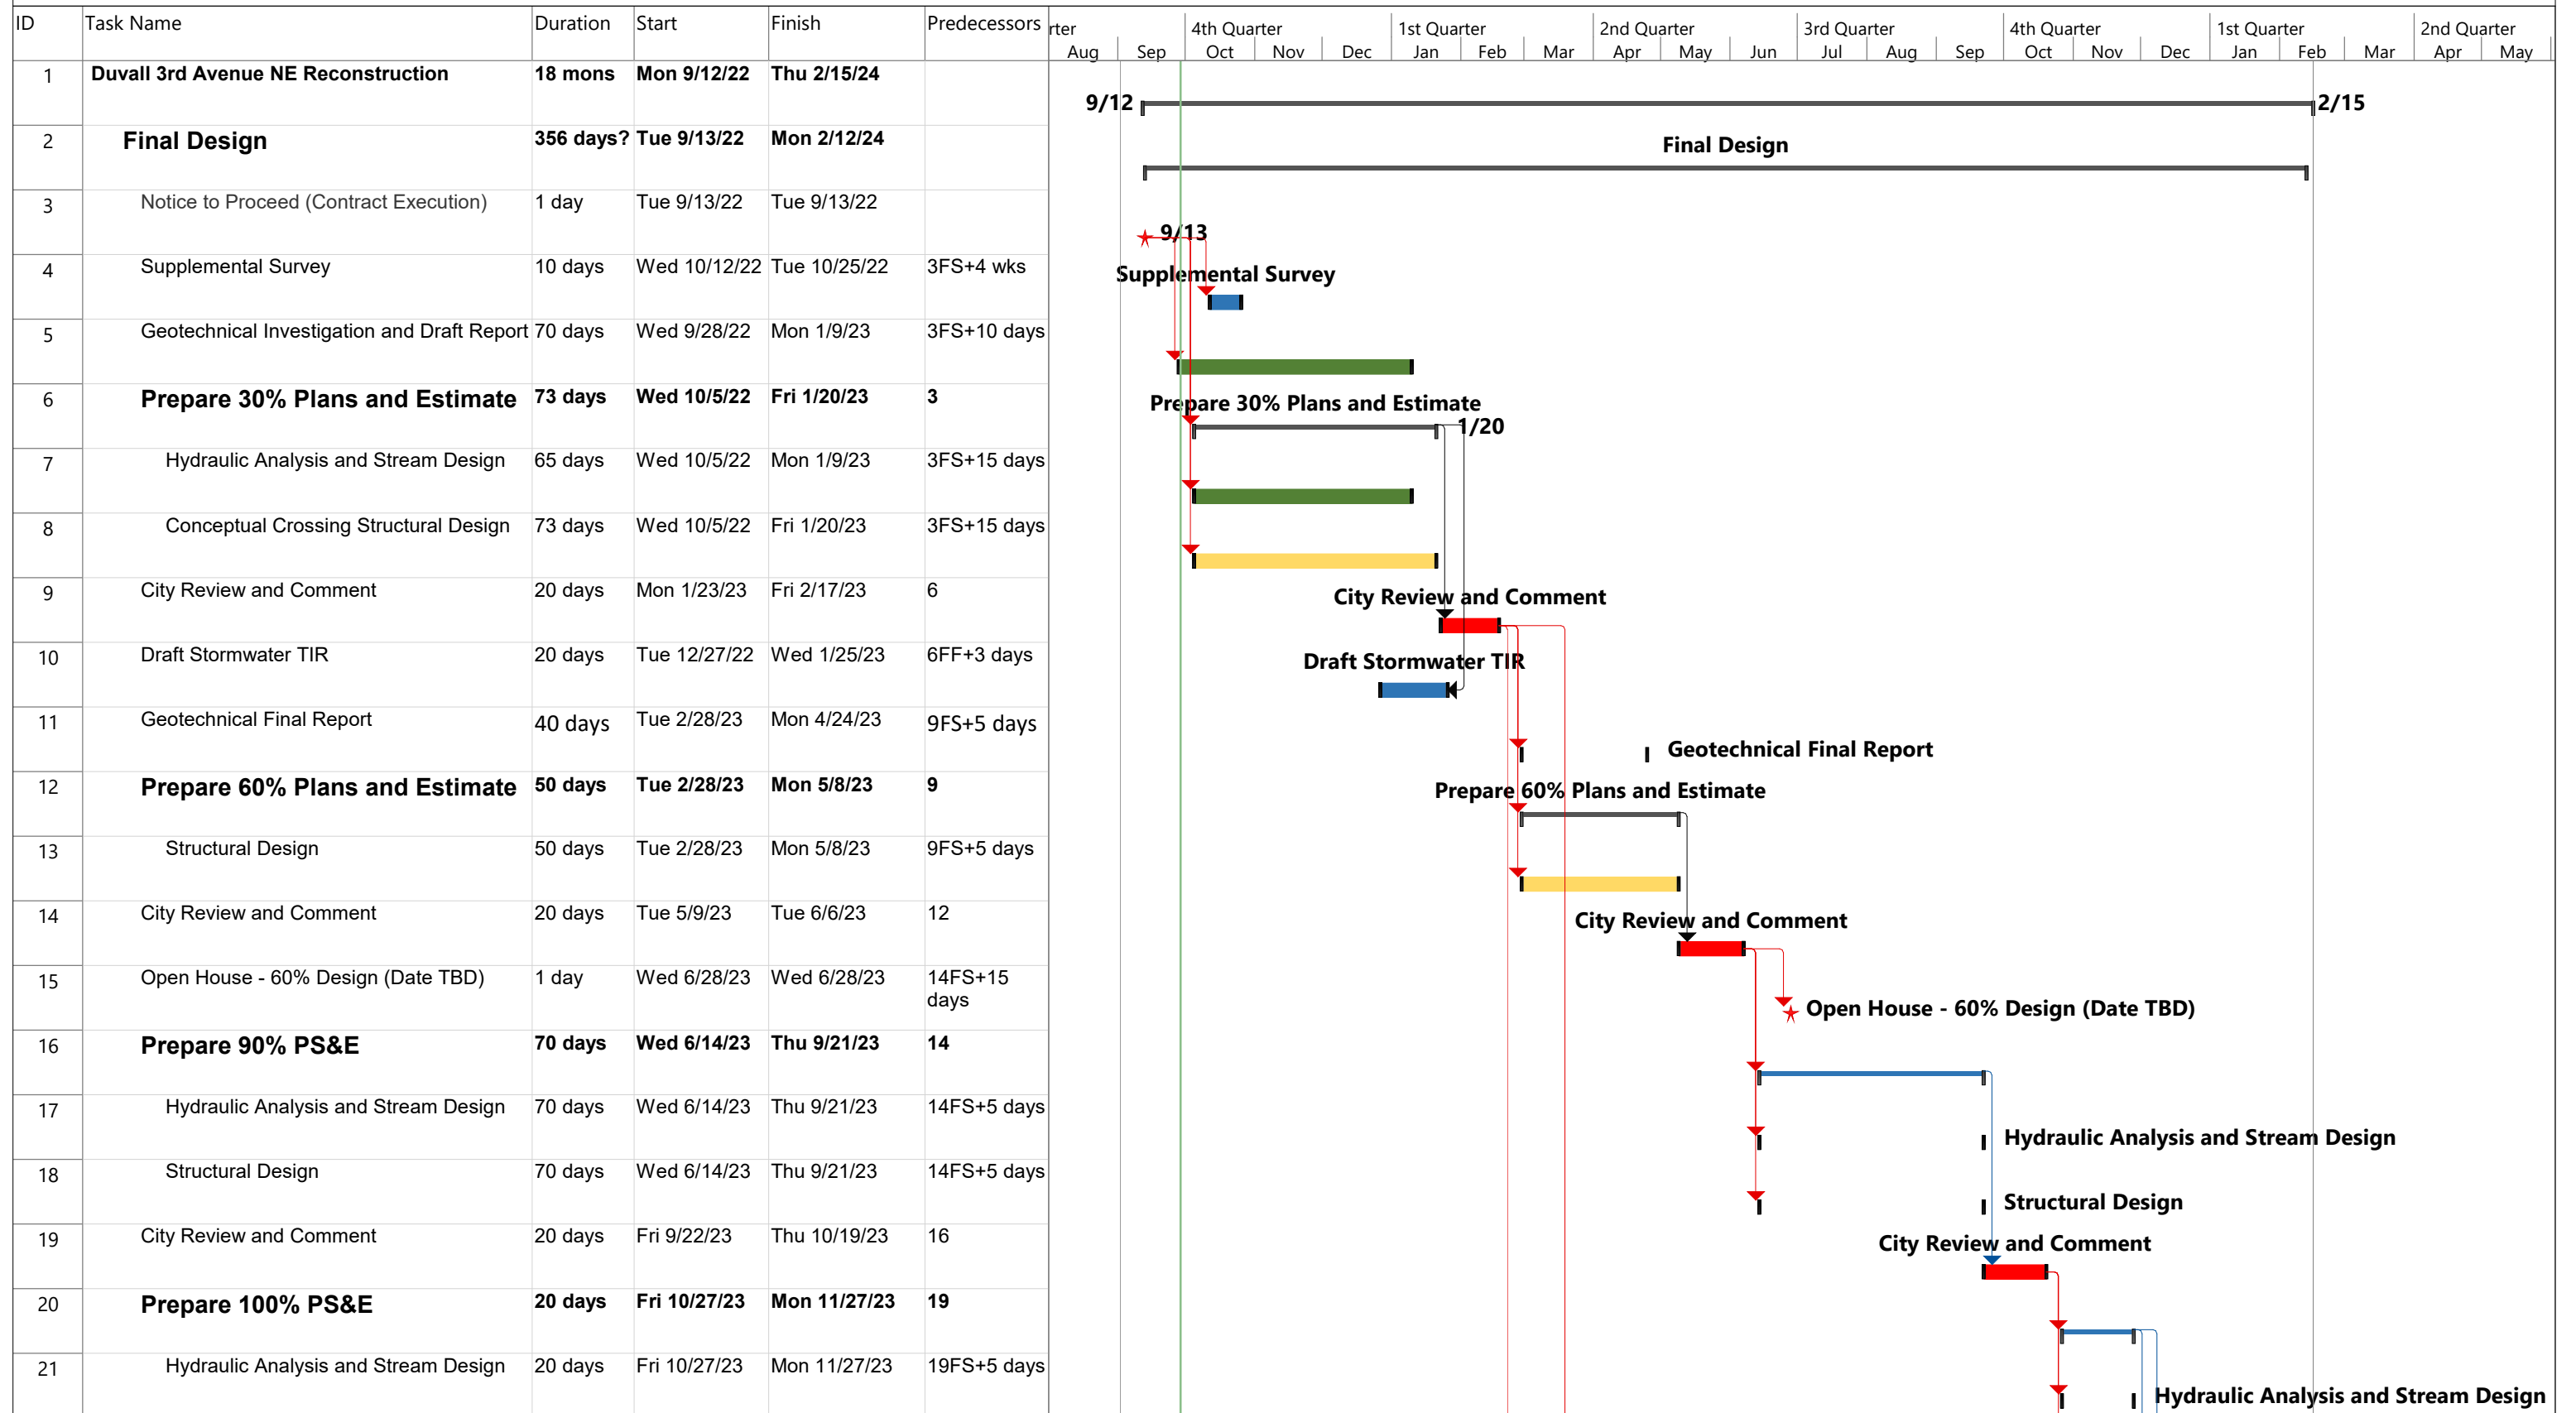
